

ONE TRUE STORY, THEN THE NETWORK AROUND IT

# Six months, five phases, one dependency chain.



Every phase is scoped from what the code does today, and sequenced so each one unblocks the next. Windows are planned execution ranges: phase N+1 starts when phase N's definition of done is met, not on a calendar trigger.

| HORIZON             | OWNER       | BASELINE          | REVISED    |
|---------------------|-------------|-------------------|------------|
| Aug 2026 → Jan 2027 | kurodenjiro | product-status.md | 2026-08-19 |

## BASELINE — READ OUT OF THE CODE, NOT THE PITCH

### WORKS END TO END

Mesh — libp2p, mDNS, gossipsub  
BLE offline plane — iOS, Android  
Intent lifecycle, compose to proof  
Escrow live on Avalanche Fuji  
Offline signing + relay queue  
Vault — AES-256-GCM  
Guardian mesh unlock


### UI EXISTS, BEHAVIOUR DOES NOT

PRIVACY — parsed, no routing code  
MODE — labels, no strategy differs  
SWAP / STAKE — every path is Escrow  
USDC · WETH · BTC.b — never funded

### NOT WIRED UP AT ALL

AI negotiation — called nowhere  
Marketplace — contracts inert  
ZK — no proving code in the build  
FHE / MPC — no code exists  
Recovery delay + veto  
Mobile PIN — blocked on ticket 21

## TIMELINE

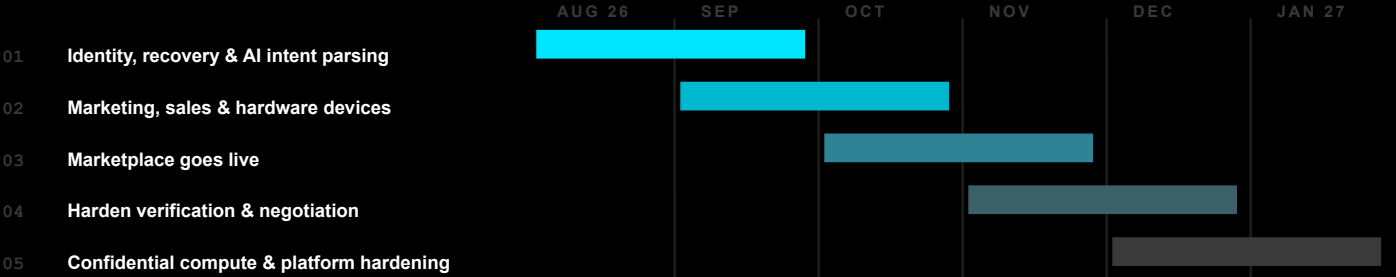

## PHASES — GOAL AND DEFINITION OF DONE

|    |                                                                                                                                                                                                                                                                                                                                                                |                     |             |
|----|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------|-------------|
| 01 | <b>Identity, recovery &amp; AI intent parsing</b><br>Close the lose-the-device risk; turn typed language back into a validated intent draft.<br><i>DONE WHEN</i> — A wiped device restores from 3-of-5 guardians with a live 24h veto window on real hardware, and a typed intent parses into editable chips.                                                  | AUG – SEP 2026      | IN PROGRESS |
| 02 | <b>Marketing, sales &amp; hardware devices</b><br>ShadowBox and the Nobody Box as concept products, plus a pre-order channel. Marketing/BD, not firmware.<br><i>DONE WHEN</i> — Both devices have finished renders, a pre-order page is live, and one campaign reaches beyond current testers.                                                                 | SEP – OCT 2026      | NEXT        |
| 03 | <b>Marketplace goes live</b><br>Relay traffic → MB → AVAX → modules → higher relay yield. Fix mintVoucher access control first.<br><i>DONE WHEN</i> — A user earns MB from real gateway relaying, converts it to AVAX, and equips a module that visibly changes relay yield on HOME.                                                                           | OCT – NOV 2026      | NEXT        |
| 04 | <b>Harden verification &amp; negotiation</b><br>Make the ZK and AI claims true end to end: write the circuit and the proving path, and enforce guardrails in Rust.<br><i>DONE WHEN</i> — A bid's proof is generated and verified against a real circuit from a command the app calls; two agents complete a bounded negotiation without breaching a guardrail. | NOV – DEC 2026      | LATER       |
| 05 | <b>Confidential compute &amp; platform hardening</b><br>FHE/MPC feasibility, desktop key store, and the Windows/Linux BLE decision.<br><i>DONE WHEN</i> — A feasibility write-up and a scoped follow-on plan for FHE/MPC — not shipped code.                                                                                                                   | DEC 2026 – JAN 2027 | EXPLORATORY |

## RISKS & BLOCKERS

|                                                                                                                      |    | NEXT 30 / 60 / 90 |                                                                                                                                      |
|----------------------------------------------------------------------------------------------------------------------|----|-------------------|--------------------------------------------------------------------------------------------------------------------------------------|
| <b>No physical iOS/Android test device</b><br>Borrow test hardware before Phase 1 is called done.                    | P1 | 30 DAYS           | — 24h recovery delay + veto notification<br>— Scope ticket 21 as its own workstream<br>— Hide SWAP / STAKE and unfunded assets       |
| <b>Native key-store plugin (ticket 21)</b><br>Own workstream; a PIN needs a hardware retry counter.                  | P1 |                   |                                                                                                                                      |
| <b>No manufacturing partner</b><br>Phase 2 runs as marketing/BD; renders do not need it.                             | P2 | 60 DAYS           | — Ship editable chips, QA the chat-intent flow<br>— Recovery assistant for lost devices<br>— Finish renders, draft landing-page copy |
| <b>Voucher redeploy is one-way</b><br>Explicit go/no-go. Testnet, no value locked today.                             | P3 |                   |                                                                                                                                      |
| <b>No ZK code, no nargo in CI</b><br>The unused stub was deleted; budget Phase 4 to write the circuit, not wire one. | P4 | 90 DAYS           | — Launch pre-order page + first campaign<br>— Run mesh missions, mint Genesis badges<br>— Draft the voucher redeploy go/no-go        |
